



# **Risk Management at CSA – An Overview**


## **NASA Risk Management Conference 2005**

File: Risk Brief to NASA Risk Management Conference Dec 2005.ppt



Canadian Space Agency  
Agence spatiale  
canadienne

**Canada**





# Presentation Contents

---

- CSA Corporate Overview
- Historical Background of RM at CSA
- RM today at CSA




Canadian Space Agency  
Agence spatiale  
canadienne

Canada

**SERVING CANADIANS FOR OVER 40 YEARS...**  
SERVING CANADIANS FOR OVER 40 YEARS...



**Alouette**



**Anik Series**



**Hermes**




**Canadarm**

## The Canadian Space Agency's Mandate

- "...to promote the peaceful use and development of space, to advance the knowledge of space through science and to ensure that space science and technology provide social and economic benefits for Canadians."





# PROFILE

CANADIAN SPACE AGENCY

- Annual budget of about \$300M (75% contracted out to industry and academia)
- Approximately 600 employees, 240 students annually
- Headquarters: John H. Chapman Space Centre (Longueuil, Quebec)
- Offices in Ottawa, Washington, Paris, Houston
- Testing & Integration Facilities at David Florida Laboratory, Ottawa

# QUALIFIED TEST & OPERATIONS INFRASTRUCTURES


QUALIFIED TEST & OPERATIONS INFRASTRUCTURES



**The David Florida Lab**


# CORE THRUSTS

- **Earth Observation**
- **Space Science and Exploration**
- **Satellite Communications**
- **Space Awareness and Learning**



## Monitoring the health of our planet from space

- Measuring pollution
- Studying ozone depletion
- Ensuring the stewardship of our natural resources
- Improved weather forecasting
- Monitoring natural disasters
- Sovereignty and security

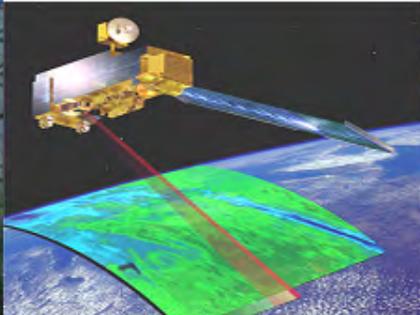


**EARTH OBSERVATION**





## **RADARSAT-1 – Assisting those in need**

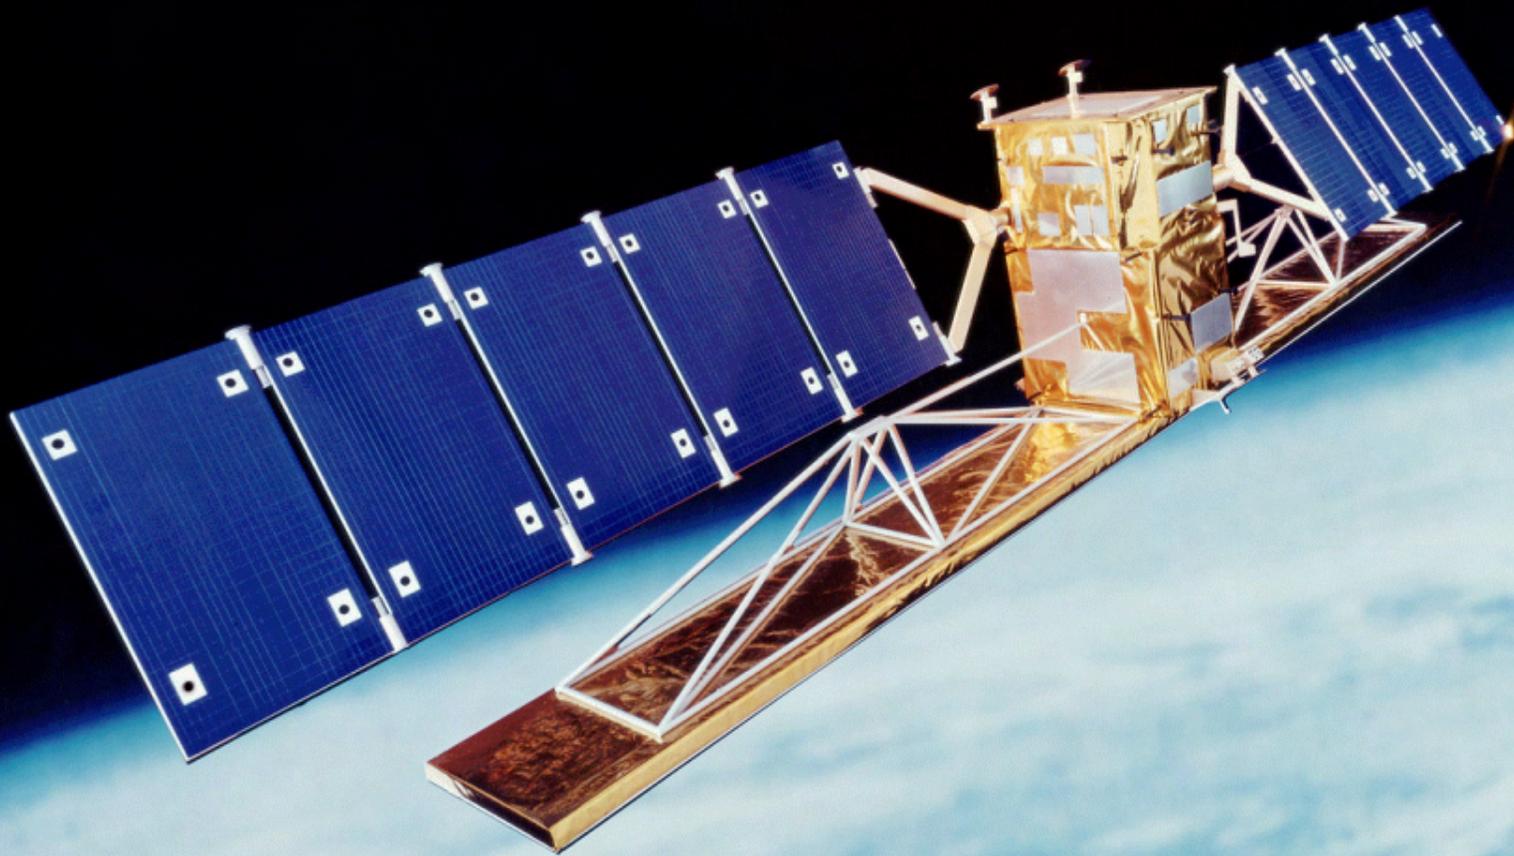


# RADARSAT-2

RADARSAT-2

Helping to keep  
Canada among the  
leaders in space-  
based, remote  
sensing technologies




SCISAT  
SCISAT

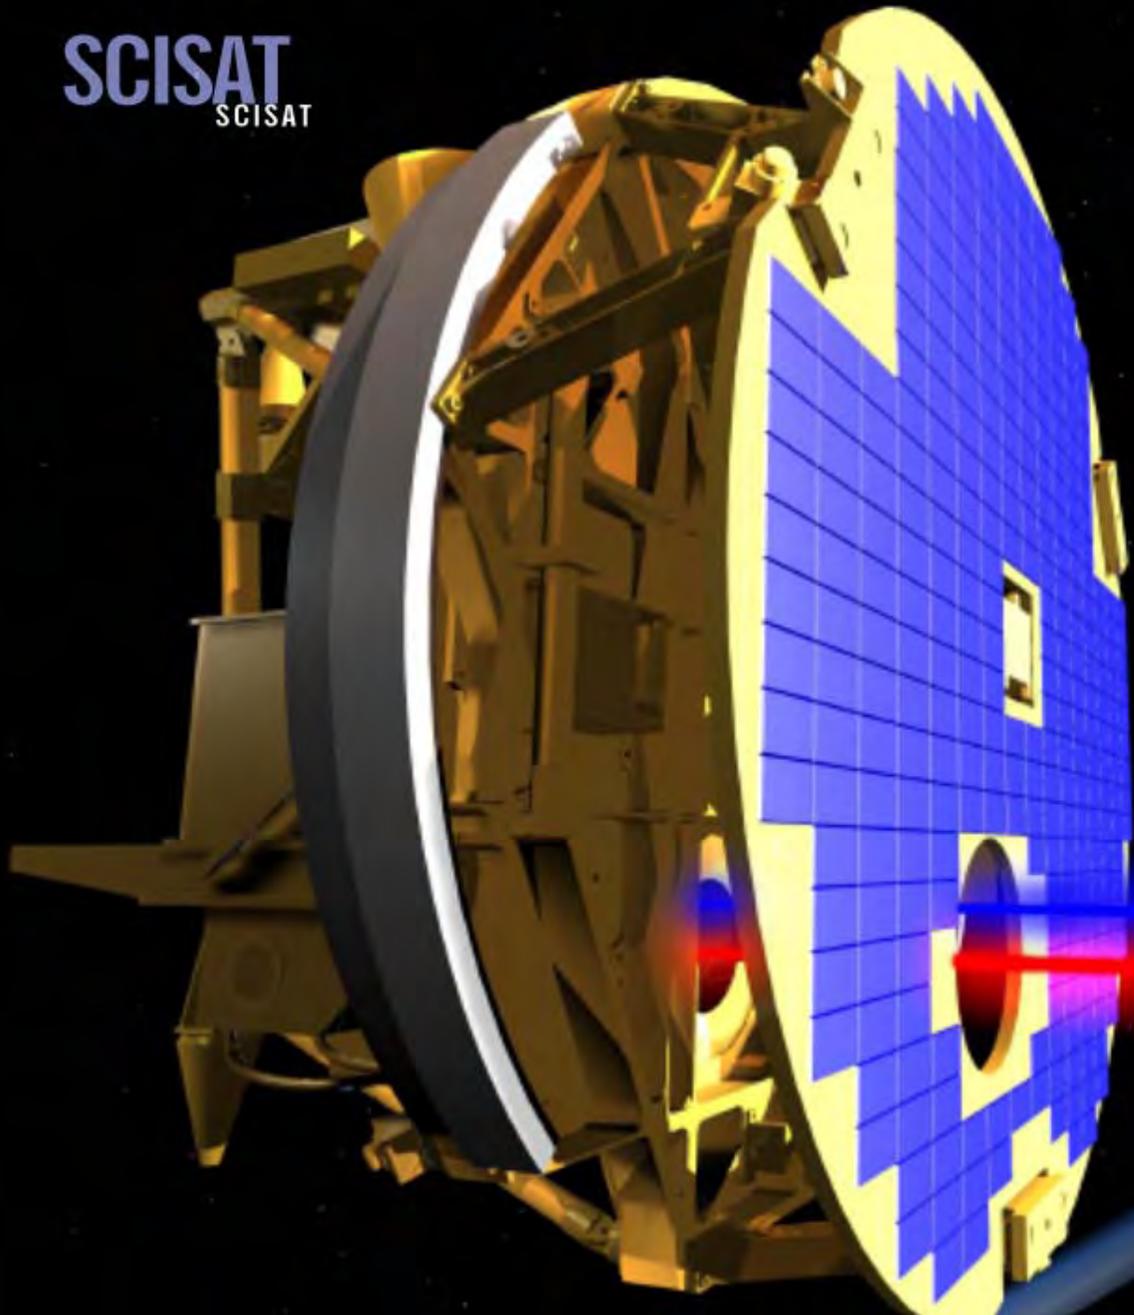

**CLOUDSAT**  
CLOUDSAT



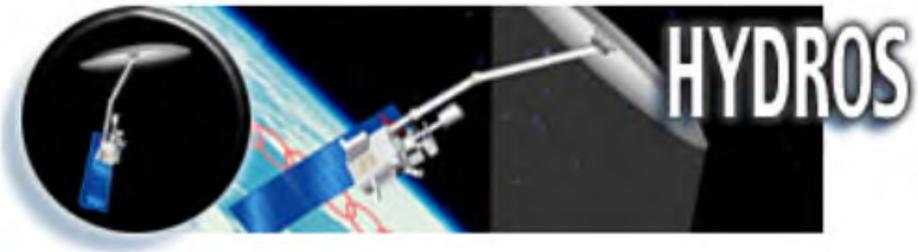

**HYDROS**



# CONNECTING CANADIANS

CONNECTING CANADIANS



ANIK F2



**CASSIOPE**  
CASSIOPE



# SPACE SCIENCE & EXPLORATION

SPACE SCIENCE & EXPLORATION



# THE INTERNATIONAL SPACE STATION


THE INTERNATIONAL SPACE STATION



# THE INTERNATIONAL SPACE STATION

THE INTERNATIONAL SPACE STATION

## Mobile Servicing System

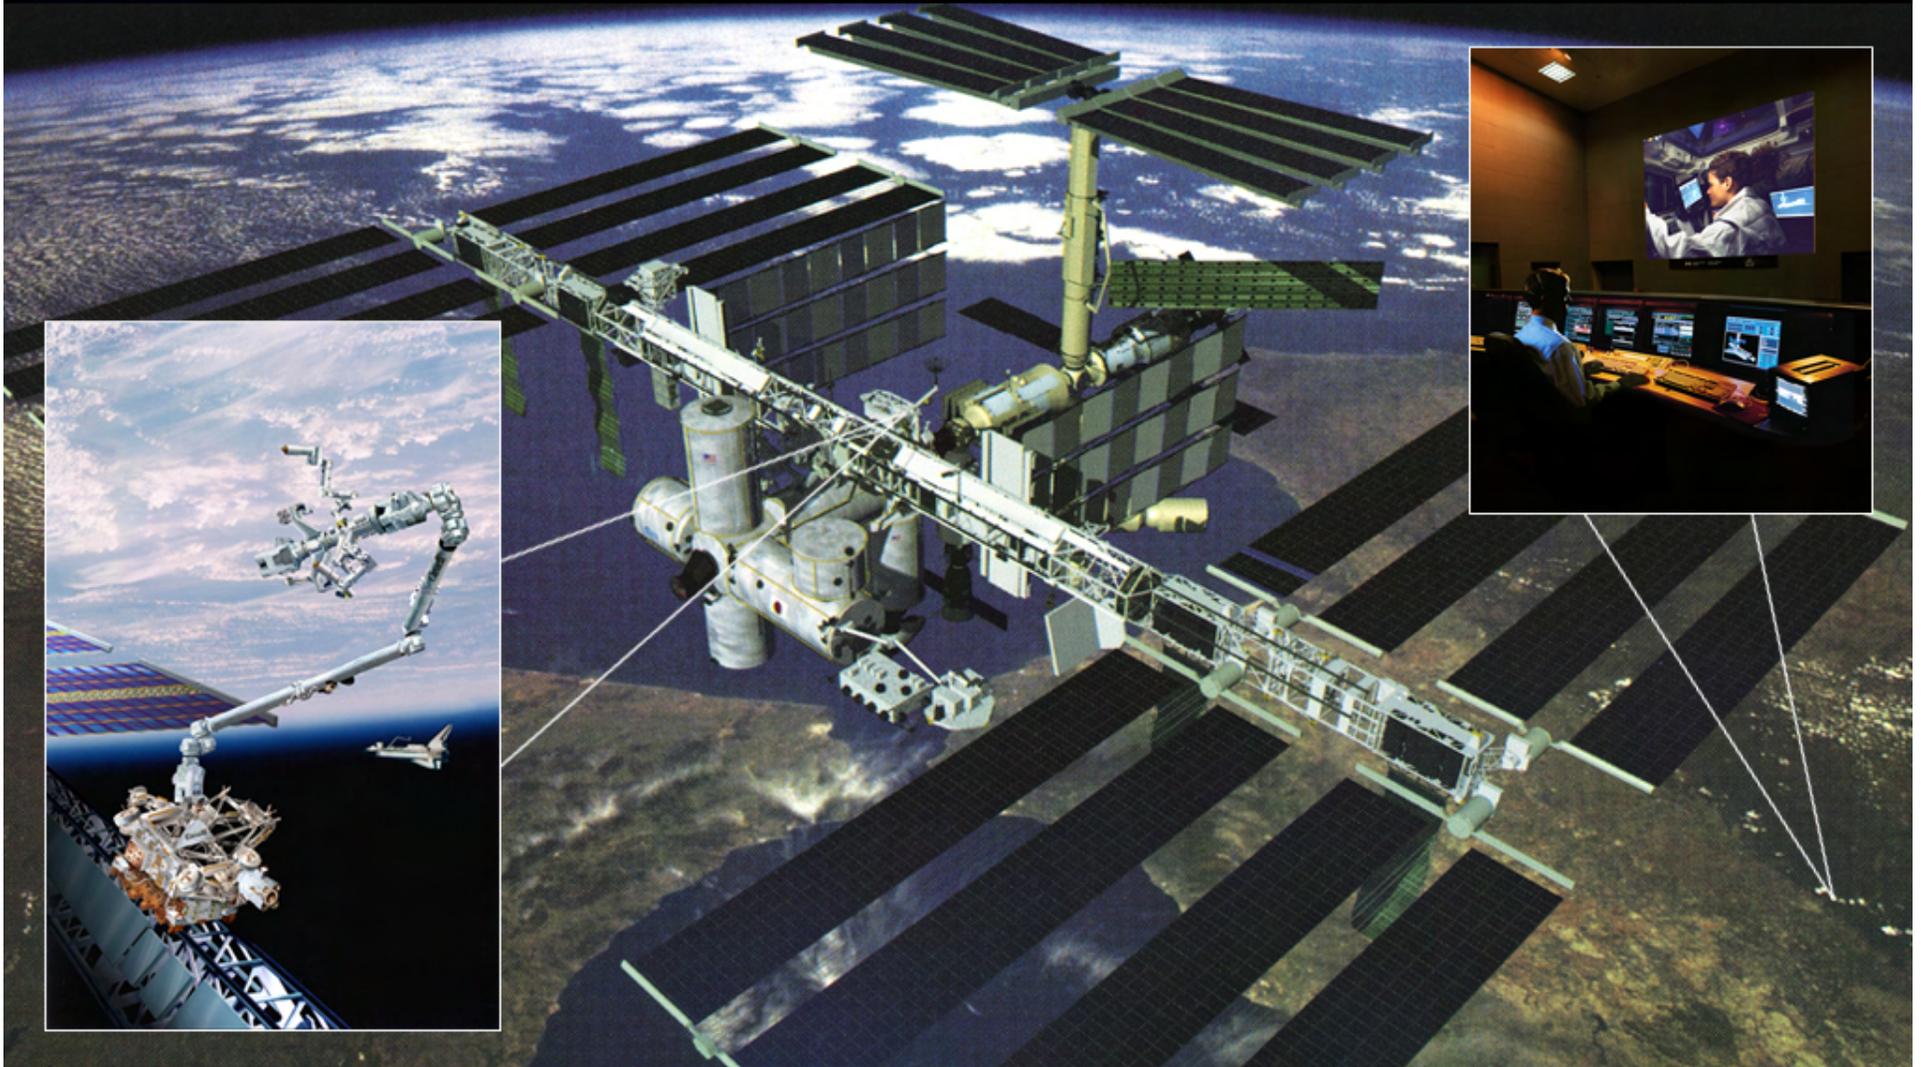

# A WORLD-RENOINED TEAM OF ASTRONAUTS

A WORLD-RENOINED TEAM OF ASTRONAUTS




Garneau '84  
Bondar '92  
MacLean '92  
Hadfield '95  
Garneau '96  
Thirsk '96  
Tryggvason '97  
Williams '98  
Payette '99  
Garneau 2000  
Hadfield 2001  
**MacLean**  
**Williams**


# SPACE SCIENCE & EXPLORATION

SPACE SCIENCE & EXPLORATION

## Astronomy and the Solar System

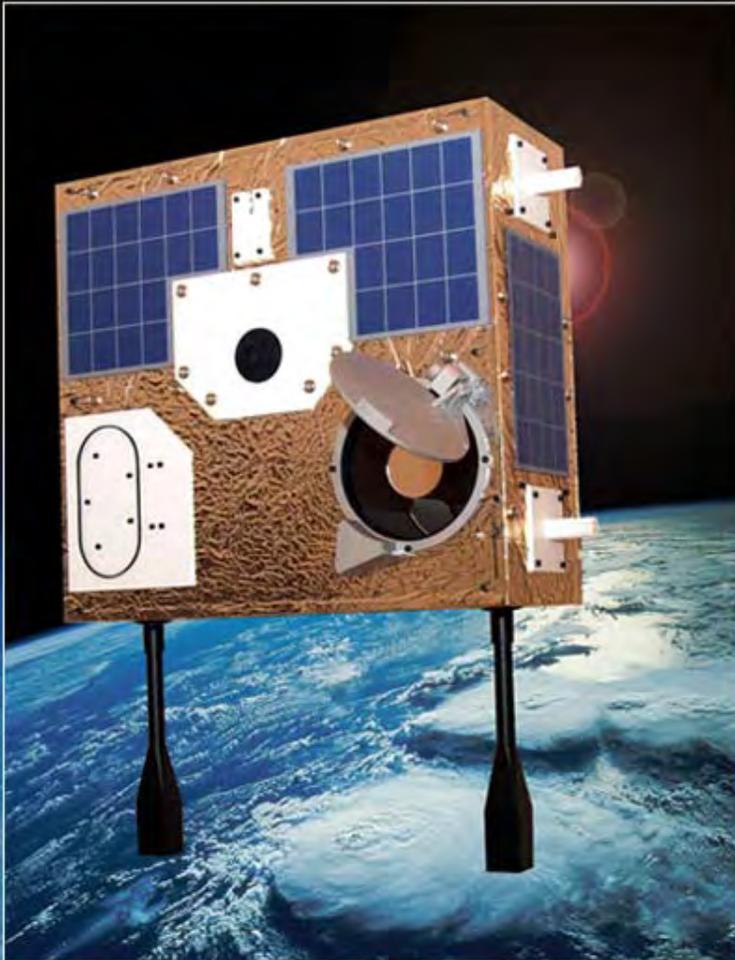


MOST

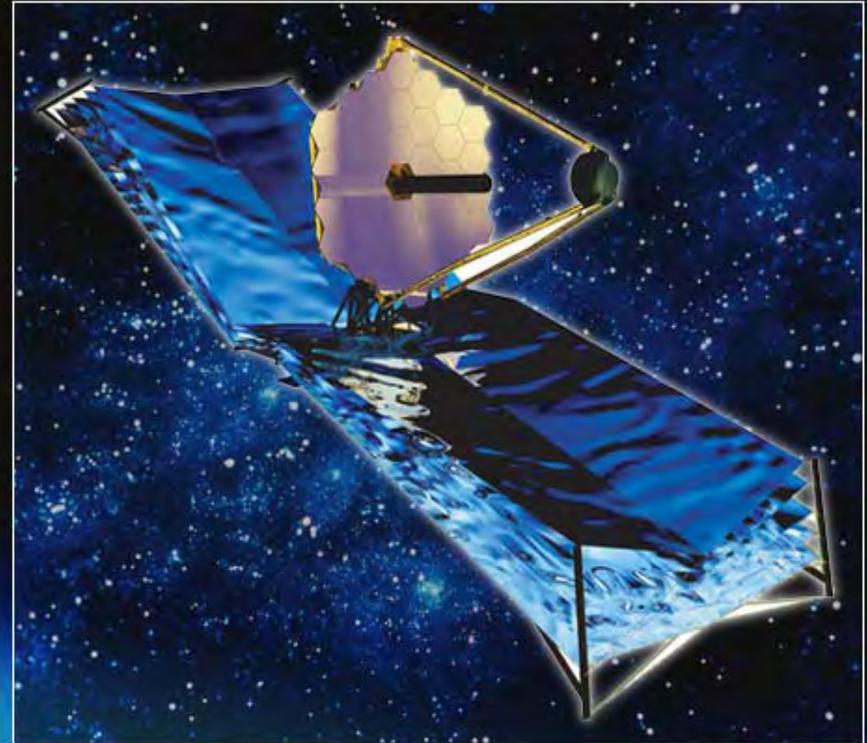


JWST


**MARS**  
MARS

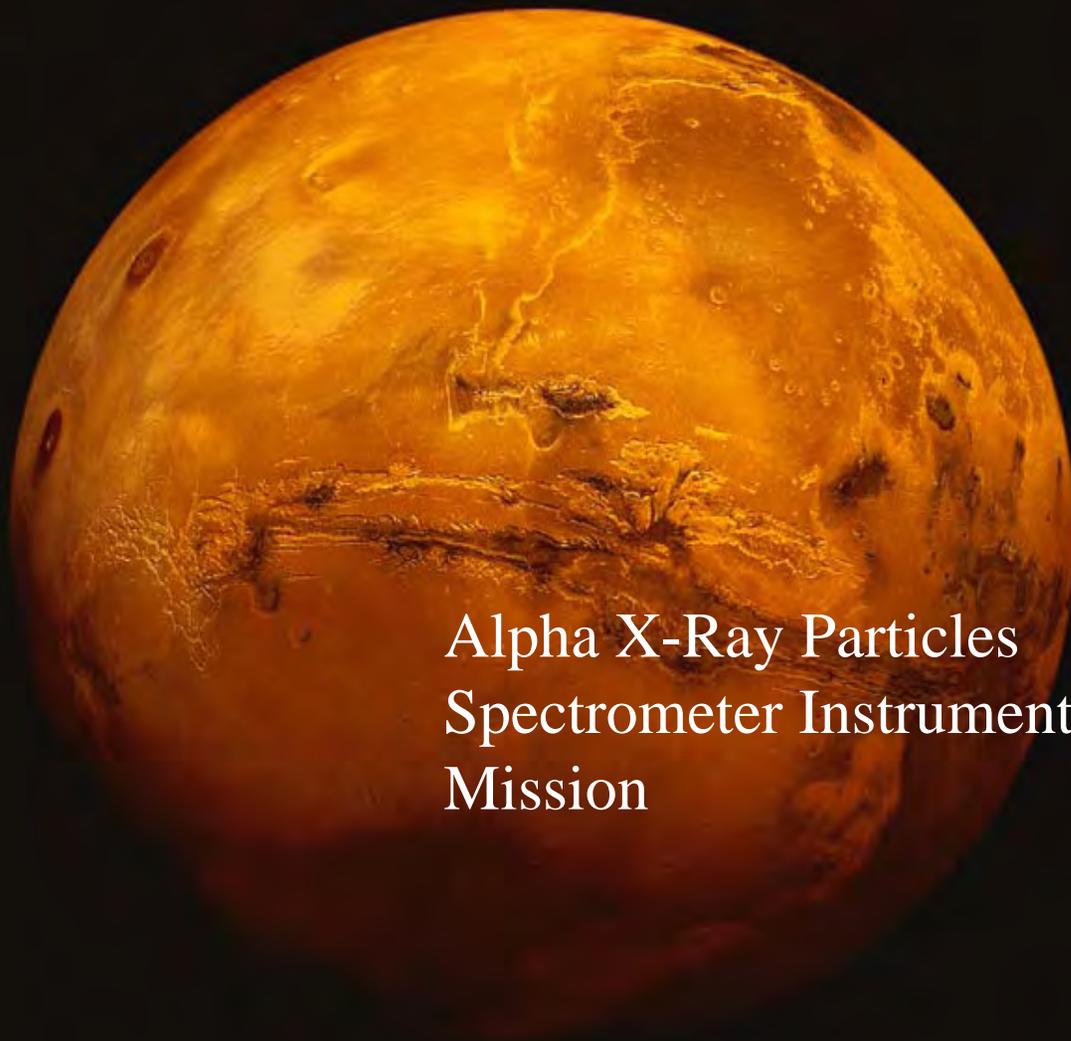

Alpha X-Ray Particles  
Spectrometer Instrument on MSL  
Mission



MET Station (LIDAR with  
Pressure and Temperature sensing  
Instrument) on Phoenix Mission

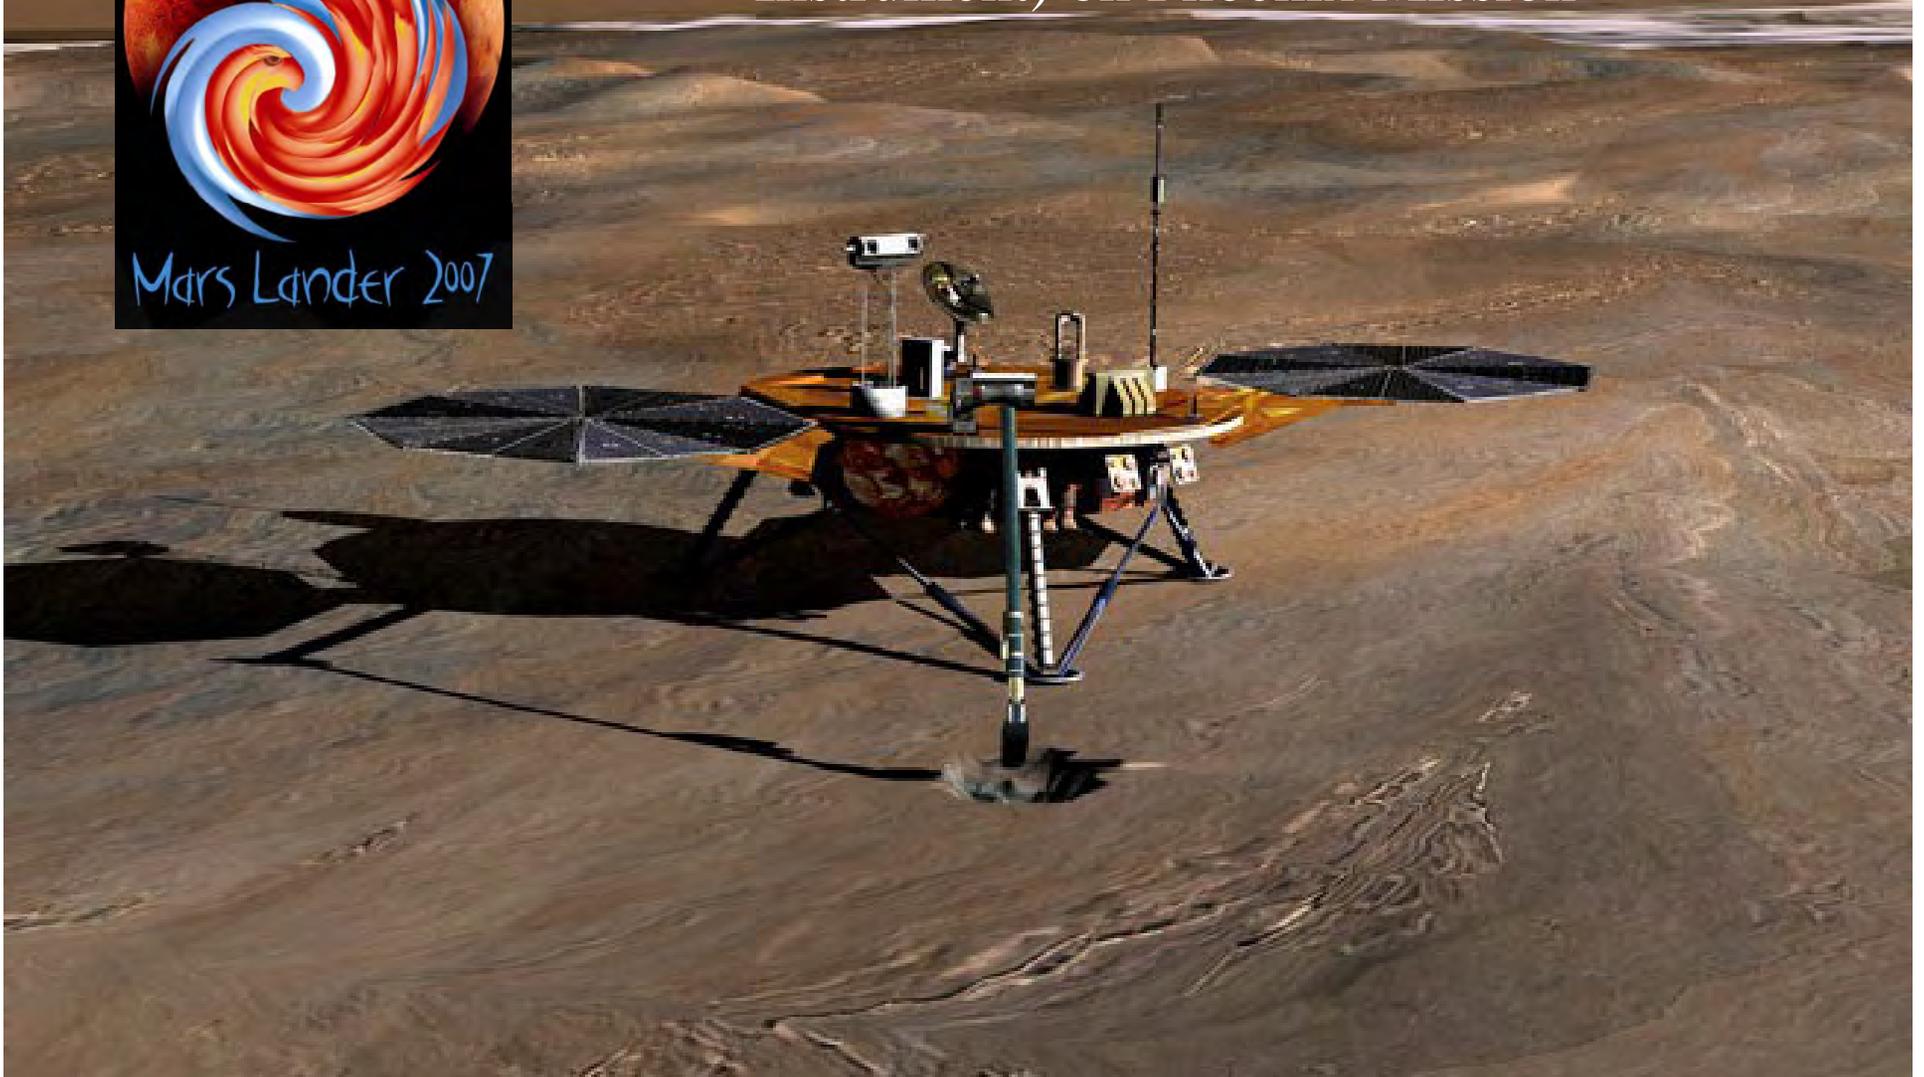

# Historical Background of RM at CSA

---



## 1989 - CSA created

- Two Major Projects (CSSP & RDST-1) influenced CSA Project Management development
- As well as TB, DND and NASA, in particular
- But also other space agencies, IAF, OGDs, industry partners and PMI

## 1994 - RIAS was developed for CSSP

- Risk identification and assessment system
- Consistent with NASA terminology and reporting

## 1996 - CSA re-org with 2 Risk Management Focus Groups

- Finance Directorate: CSA Cost Risk
- Space Programs: Project Risk Management

# Historical Background of RM at CSA



---

## After 1996

- ⌚ Planning, Reporting, Accountability Structure (PRAS) (plus overall fixed yearly funding)
- ⌚ CSA RMF (plus internal project approval of \$1M)
- ⌚ PAMF (and increased delegated authority to \$5M)
- ⌚ Results for Canadians
- ⌚ Modern Comptrollership
- ⌚ CSSP Project close out report (Lessons Learned)
- ⌚ Audit's Report
- ⌚ Management Accountability Framework (MAF)



# Historical Background of CSA

---




2001 – Marc Garneau was appointed as the CSA president

A number of re-organization followed:


- CSA moved from a former Major Crown Project structure to a Matrix structure
- Systems Engineering moved from Sp. Pgms (formerly Sp. Systems) directorate to Sp. Tech. Directorate
- MSS Operations organisation moved from Sp. Pgms directorate to Sp. Ops directorate
- Risk Management and S&MA organisations remained under Sp. Pgms directorate

# CSA Organisation Top Level

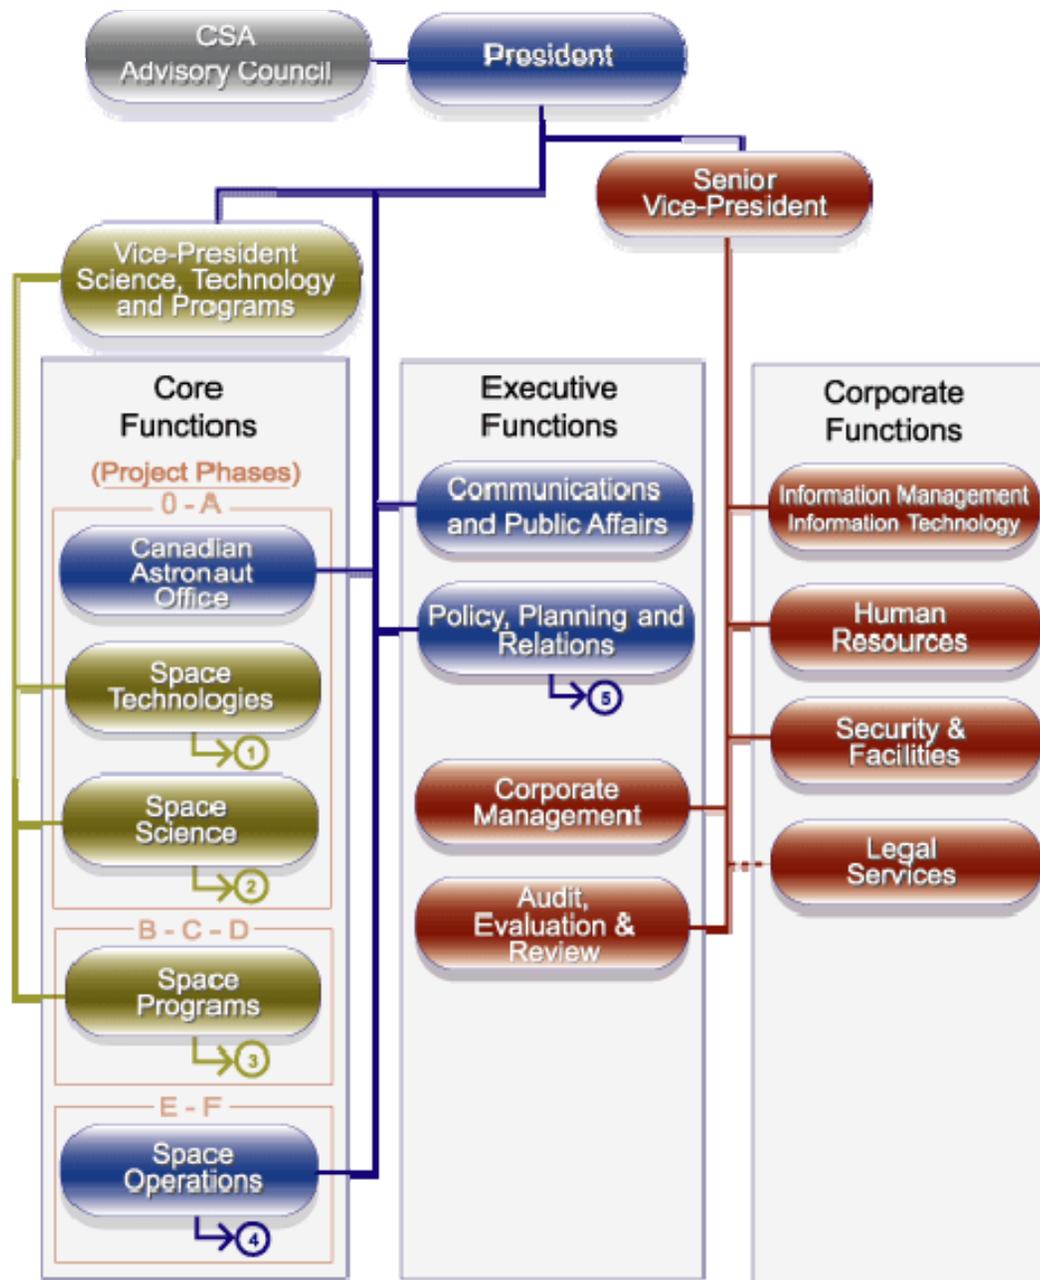




# CSA Core Functions

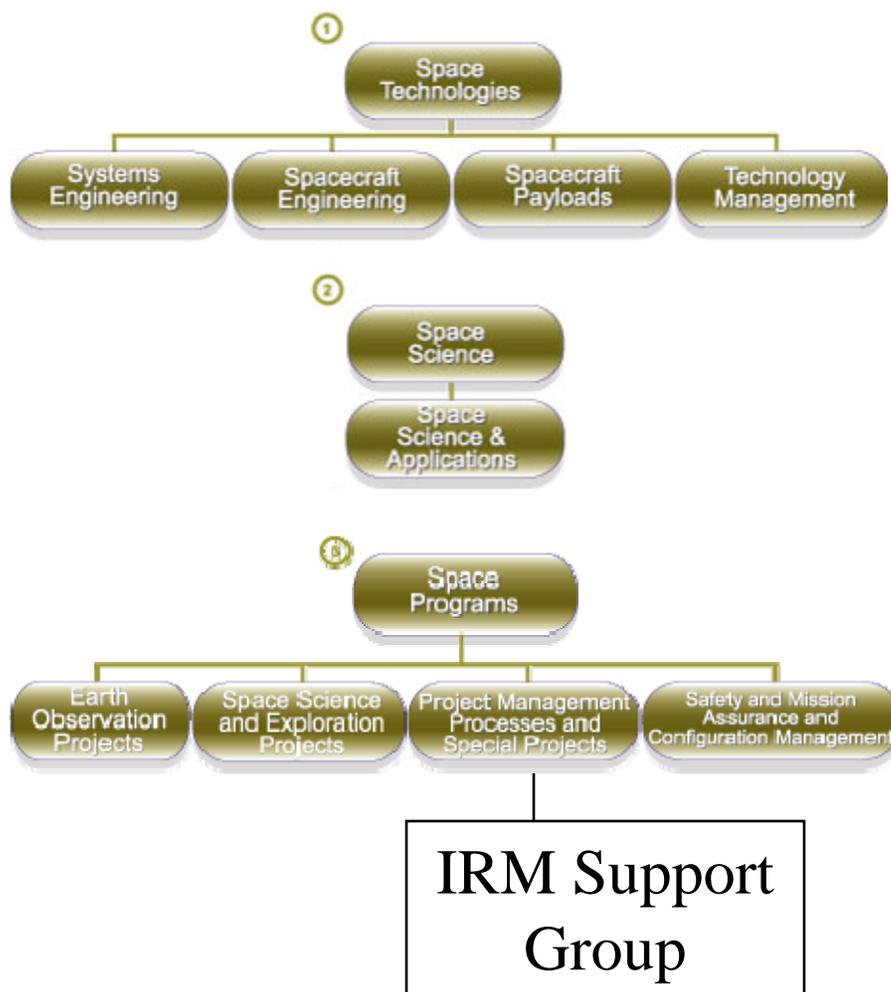

# RM today at CSA



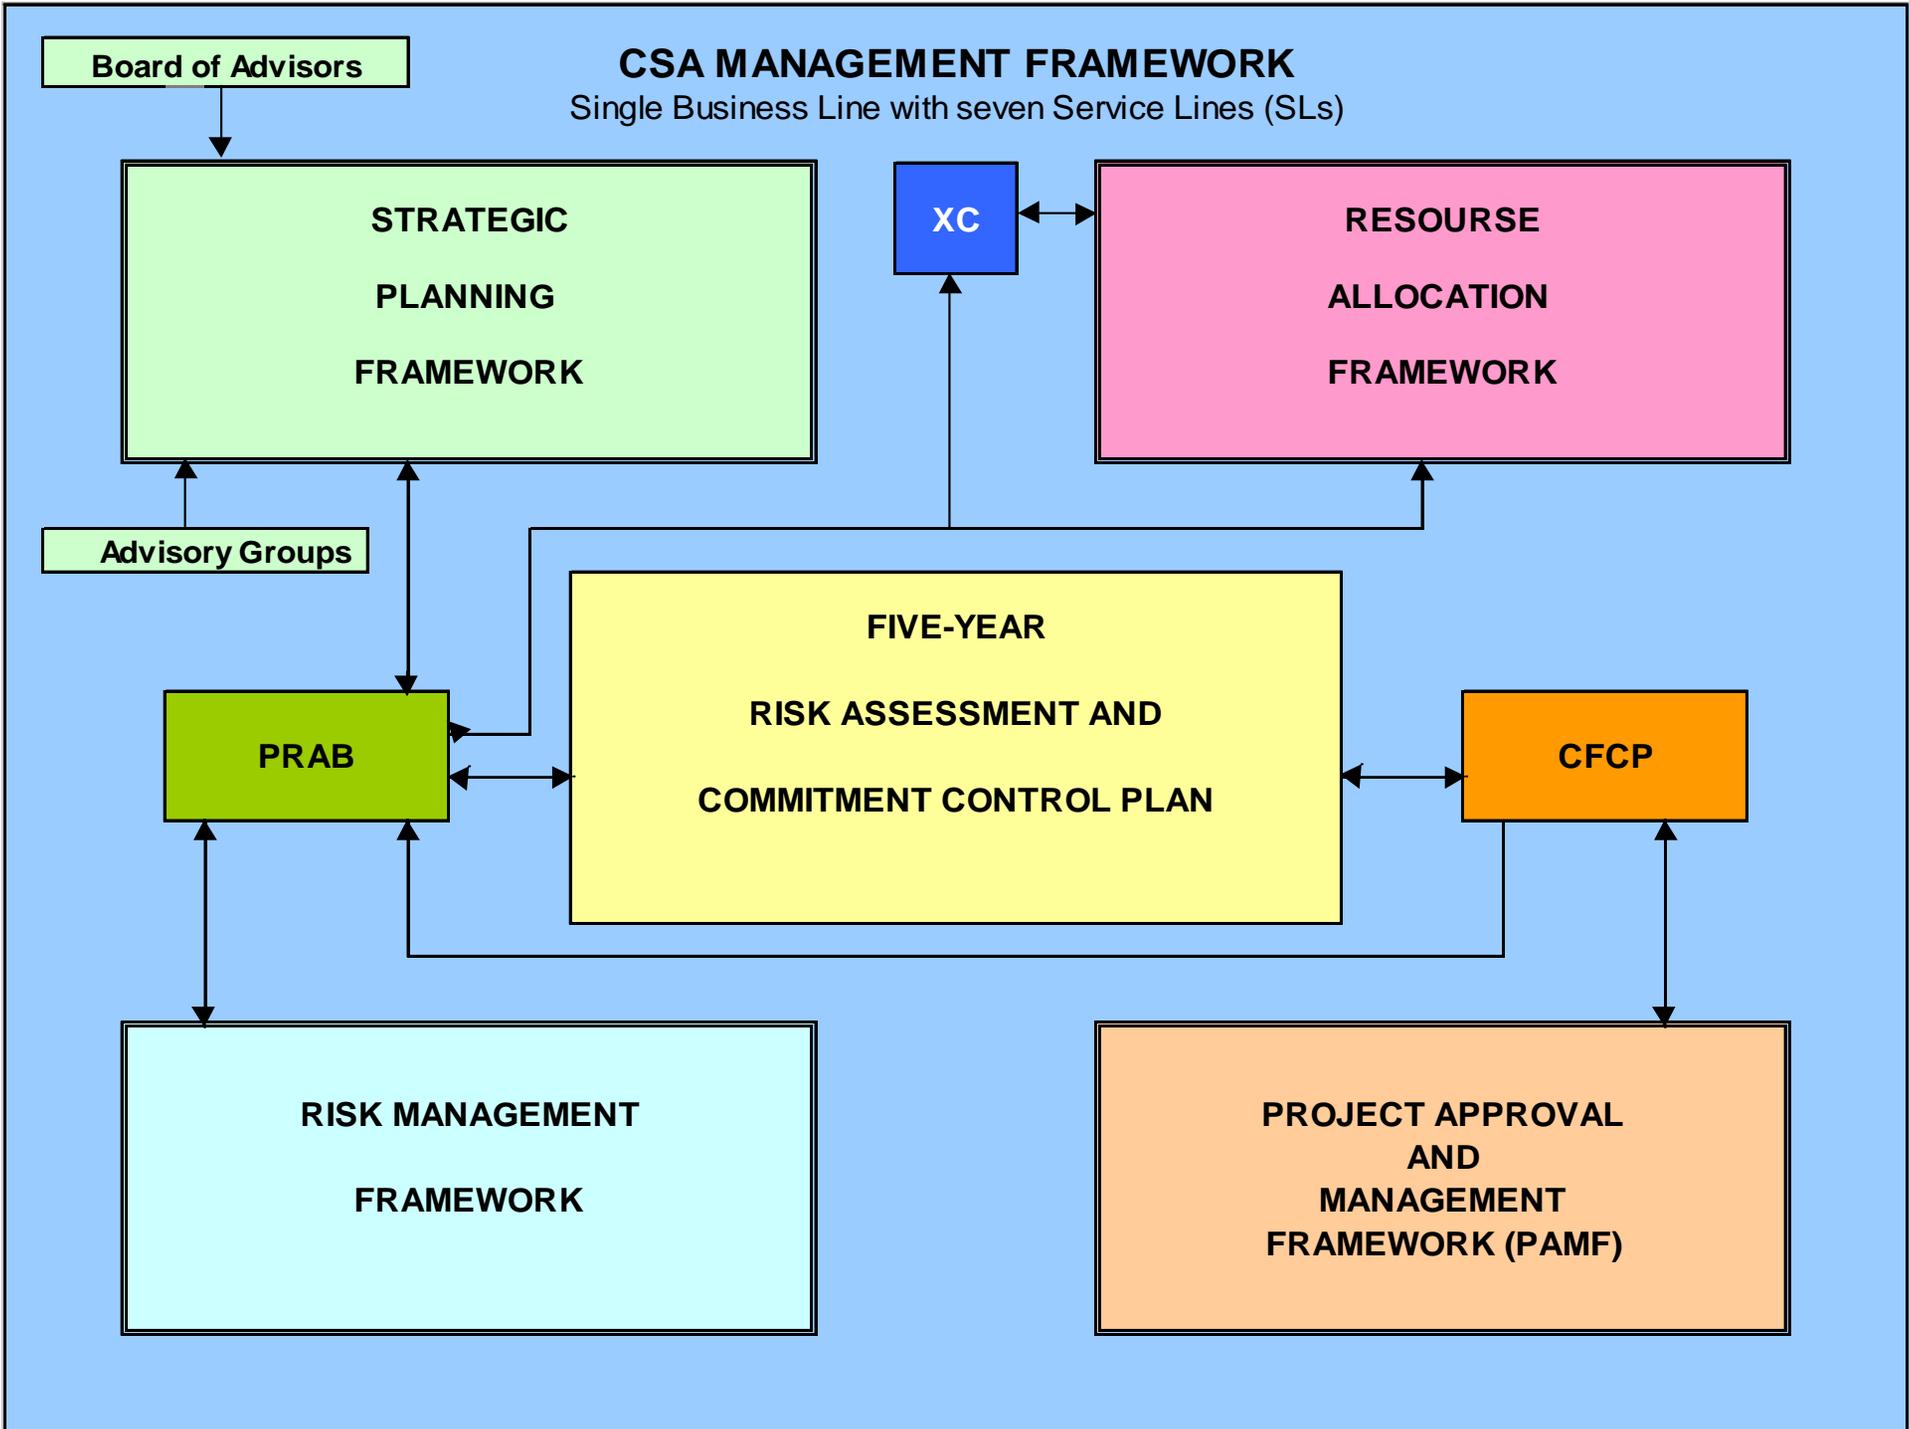



# Risk Management Framework

---

- RMF was approved by TB in December 1999, in the context of the government decision to endow CSA with a stable A-Base budget
- To ensure that the Canadian Space Program and associated risks can be funded within the Multi-Year Approved Reference Levels
- As a result, new initiatives are funded only when ongoing program risks are under control

# Risk Management Framework

---



Key to the CSA Risk Management Framework is the integration of Risk Management into the Agency's long-term and annual planning, resource allocation and performance framework. Hence, project risk management at the CSA implies 3 levels of management;

- 1-) Corporate level including the Service Lines ( CSA integrated Risk Management )
- 2-) Project Level ( Project Risk Management )
- 3-) Work Package level ( continuous monitoring and assessment of risks ).





# PAMF RISK MANAGEMENT

---

## ■ PRM DERIVED FROM:

- 🔦 TB GUIDELINES
- 🔦 PMI PMBOK
- 🔦 CSA RISK MGT FRAMEWORK

## ■ PRM IMPLIES 3 LEVELS OF MANAGEMENT

- 🔦 ITEM MANAGER (WORK PACKAGE)
- 🔦 PROJECT MANAGER (PROJECT LEVEL)
- 🔦 CORPORATE (CSA MISSION)

## ■ PROJECT APPROVAL DOCUMENT (PAD)


- 🔦 GENERAL DESCRIPTION
- 🔦 WBS

## ■ PROJECT REVIEW ADVISORY BOARD (PRAB)





# Risk Management Support Team Organization

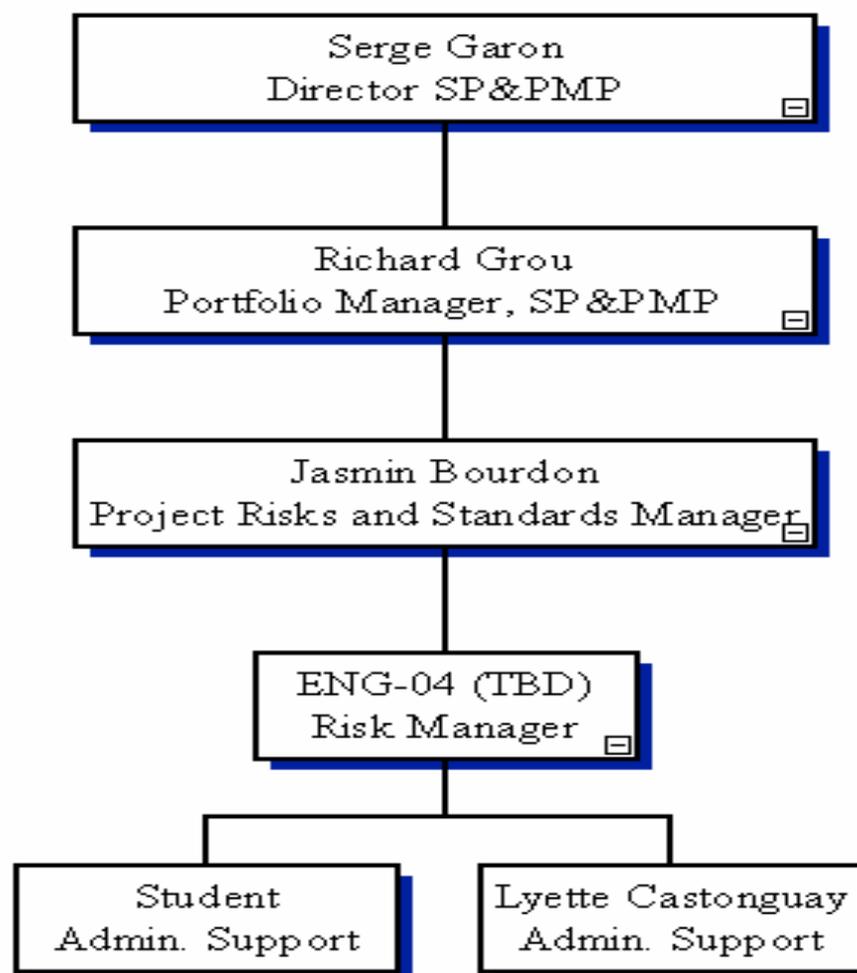



# Risk Management Support Team's Mandate

---

- Facilitate training and workshops to help project teams identify, analyze, and mitigate risks contained in project or program.
- Provide ongoing consultation, facilitation, and training, as well as formulate, select, and execute strategies to support project management decision making.
- Support the PM in monitoring project or program activities and track these activities to ensure the effectiveness of each risk-related task.

# Project Level Risk Management Process



# Activities called for in Risk Management Plans for projects


---



1. Risk Management and Strategy Planning
2. Risk Identification
3. Qualitative Risk Analysis
4. Quantitative Risk Analysis
5. Risk Response Plan
6. Risk Monitoring and Control



# CSA Integrated Risk Management Flowchart

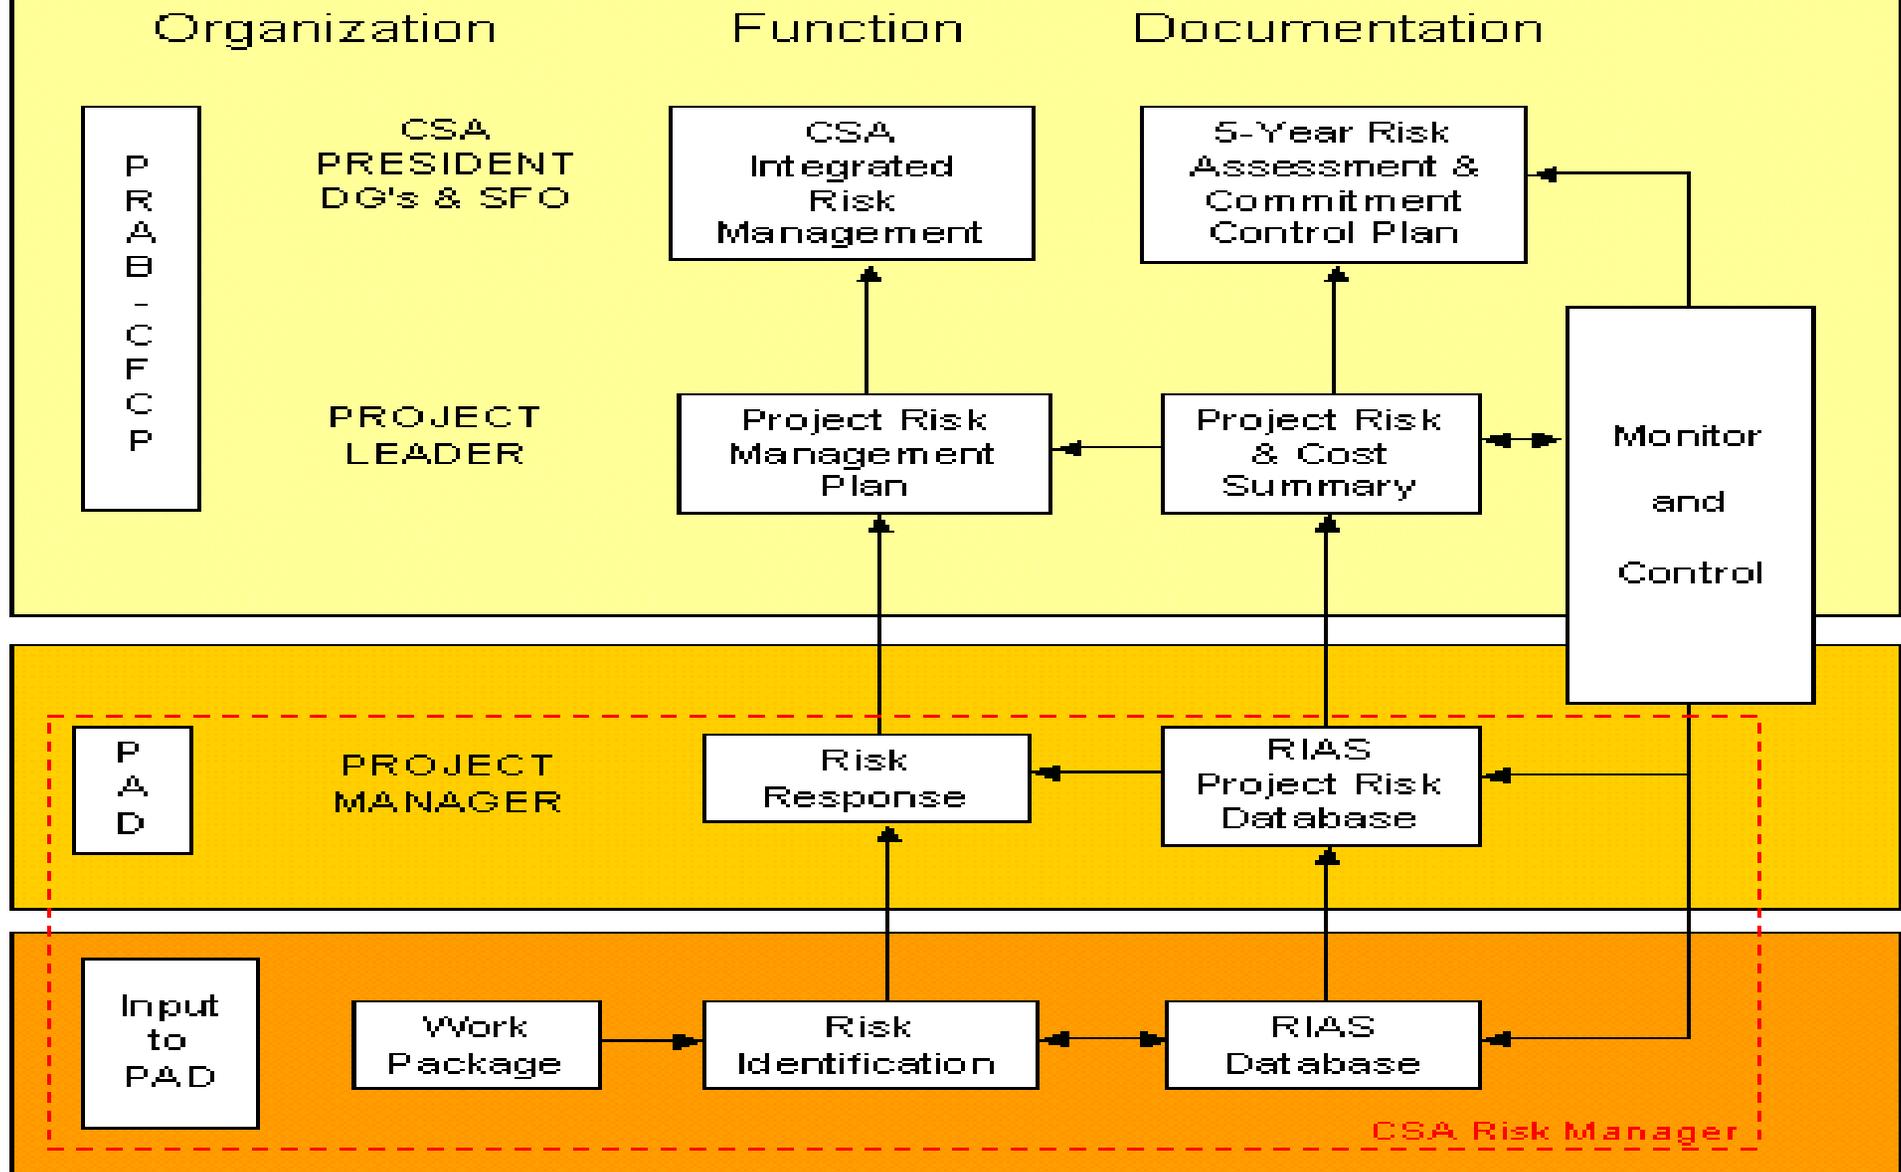

# RIAS Risk Summary Report



								<b>RISK # 01.5</b>																																								
<b>WBS Number:</b> 1.2			<b>Cost Account:</b> Phase E			<b>Risk Owner:</b> Alain Dubeau																																										
<b>Date Opened:</b> 10/25/1999		<b>Date Closed:</b>		<b>Rev #:</b> 51		<b>Last Update:</b> 09/12/2001																																										
								<table border="1"> <tr> <td rowspan="5" style="writing-mode: vertical-rl; transform: rotate(180deg);">L I K E L I H O O D</td> <td>5</td> <td style="background-color: #cccccc;"></td> <td style="background-color: #808080;"></td> <td style="background-color: #404040;"></td> <td style="background-color: #000000;"></td> </tr> <tr> <td>4</td> <td style="background-color: #cccccc;"></td> <td style="background-color: #808080;"></td> <td style="background-color: #404040;"></td> <td style="background-color: #000000; text-align: center;">○</td> </tr> <tr> <td>3</td> <td style="background-color: #cccccc;"></td> <td style="background-color: #808080;"></td> <td style="background-color: #404040;"></td> <td style="background-color: #000000;"></td> </tr> <tr> <td>2</td> <td style="background-color: #cccccc;"></td> <td style="background-color: #808080;"></td> <td style="background-color: #404040;"></td> <td style="background-color: #000000;"></td> </tr> <tr> <td>1</td> <td style="background-color: #cccccc;"></td> <td style="background-color: #808080;"></td> <td style="background-color: #404040;"></td> <td style="background-color: #000000;"></td> </tr> <tr> <td></td> <td></td> <td style="text-align: center;">1</td> <td style="text-align: center;">2</td> <td style="text-align: center;">3</td> <td style="text-align: center;">4</td> <td style="text-align: center;">5</td> </tr> <tr> <td colspan="6" style="text-align: center;">C O N S E Q U E N C E</td> </tr> </table>		L I K E L I H O O D	5					4				○	3					2					1							1	2	3	4	5	C O N S E Q U E N C E					
L I K E L I H O O D	5																																															
	4				○																																											
	3																																															
	2																																															
	1																																															
		1	2	3	4	5																																										
C O N S E Q U E N C E																																																
<b>COST EFFECT</b>	TOTAL	FY 00/01	FY 01/02	FY 02/03	FY 03/04	FY 04/05	FY 05/06	FY 06/07	FY 07/08																																							
	\$13,640.K	\$0K	\$748.571K	\$1,295.714K	\$1,817.143K	\$2,644.286K	\$3,242.857K	\$3,891.429K	\$0K																																							
<b>COST EFFECT RANGE</b>																																																
<b>SCHEDULE EFFECT</b>	1 to 6 months																																															
<b>PERFORMANCE EFFECT</b>	TBD																																															
<b>SAFETY EFFECT</b>	TBD																																															
<b>PROGRAMMATIC EFFECT</b>																																																
<b>RESPONSE PLANS</b>																																																
<b>#</b>	<b>ACTION</b>	<b>ACTIONEE</b>	<b>DATE</b>																																													
				<b>DATE</b>																																												




# RIAS Weighted Risk Report

<b>Project: Space Station</b> <b>Cost Summary Report: Weighted Cost Report - September -01 Baseline</b> <b>Date: 12-Sep-2001</b>											
Risk #	WBS Number	Cost Account	Risk Name	Risk Owner	Date Opened	Last Update	C	L	Weighting	FY 01/02 (\$'000)	WEIGHTED COST TOTAL (\$'000)
01.1	1.2.1.1-A	Phase E	Jammed Extended SSRMS with Astronaut at the End	Victor Chang	30-Apr-1998	09-Aug-2001	4	1	10%	0	100
01.3	1.1	CSSP MCP	MCP Unknown-Unknowns	Alain Dubeau	21-Oct-1999	03-Aug-2001	3	4	70%	700	1,190
01.5	1.2	Phase E	Non-MCP Unknown-Unknowns	Alain Dubeau	25-Oct-1999	12-Sep-2001	5	4	70%	524	9,548
01.9	1.2-3	Phase E	Space Station Assembly Sequence Delay	Alain Dubeau	25-May-1998	03-Aug-2001	4	1	10%	0	175
01.10	1.2.1-A	Phase E	High Contract Personnel Turnover	Benoit Marcotte	05-Jan-2000	08-Dec-2000	3	1	10%	0	250
01.11	1.2	Phase E	L&SE Contract - MD-R Default	Benoit Marcotte	20-Mar-2000	08-Dec-2000	1	1	10%	0	0
01.12	1.2.1-A	Phase E	Commercial Clients' Lawsuit against Canada due to Malfunction of Canadian ISS Components Post Launch	Alain Dubeau	07-Jan-2000	12-Sep-2001	5	1	10%	0	0
01.13	1.2	Phase E	On Call, Overtime and Shift Work	Benoit Marcotte	28-May-2000	03-Aug-2001	3	4	70%	0	560
01.14	1.2	Phase E	MDR Bankruptcy	Alain Dubeau	19-Jul-2000	12-Dec-2000	1	1	10%	0	0
01.15	1.2	Phase E	Inflation More Than Normal	Alain Dubeau	19-Jul-2000	09-Aug-2001	4	2	30%	0	600
02.1	1.1.2.2.2.2-A	CSSP MCP	Integration-Level Design Problems	Eric White	19-Apr-1996	09-Aug-2001	2	2	30%	0	30
02.3	1.2.5	Phase E	ISS MEIT II Cost Impact on CSA	Bud Coulthard	21-Oct-1999	12-Sep-2001	5	4	70%	210	210
02.4	1.2.5.5-A	Phase E	R&O Early Years	Bud Coulthard	17-Nov-1999	09-Aug-2001	5	1	10%	0	1,900
03.1	1.1.2.2.1.11-A	CSSP MCP	SSRMS Russian FGB Interface Problems	Mike Stieber	19-Sep-1996	08-Dec-2000	1	1	10%	0	0
03.3	1.2.5.3	Phase E	MSS Enhancements Due to Separate Safing	Bud Coulthard	28-May-2000	13-Mar-2001	4	5	90%	0	3,600
03.5	1.1.2.2.3.4	CSSP MCP	SPDM Ete Delay due to late delivery of OCS Build 4	Eric White	30-Jun-2000	12-Sep-2001	3	4	70%	0	350
03.6	1.2.5.3.A	Phase E	Omnibus S/W Risk - Phase E	Bud Coulthard	07-Aug-2000	04-Jul-2001	5	3	50%	0	5,000
<b>TOTALS:</b>										<b>3,154</b>	<b>39,635</b>



# RIAS Project Level Risk Matrix

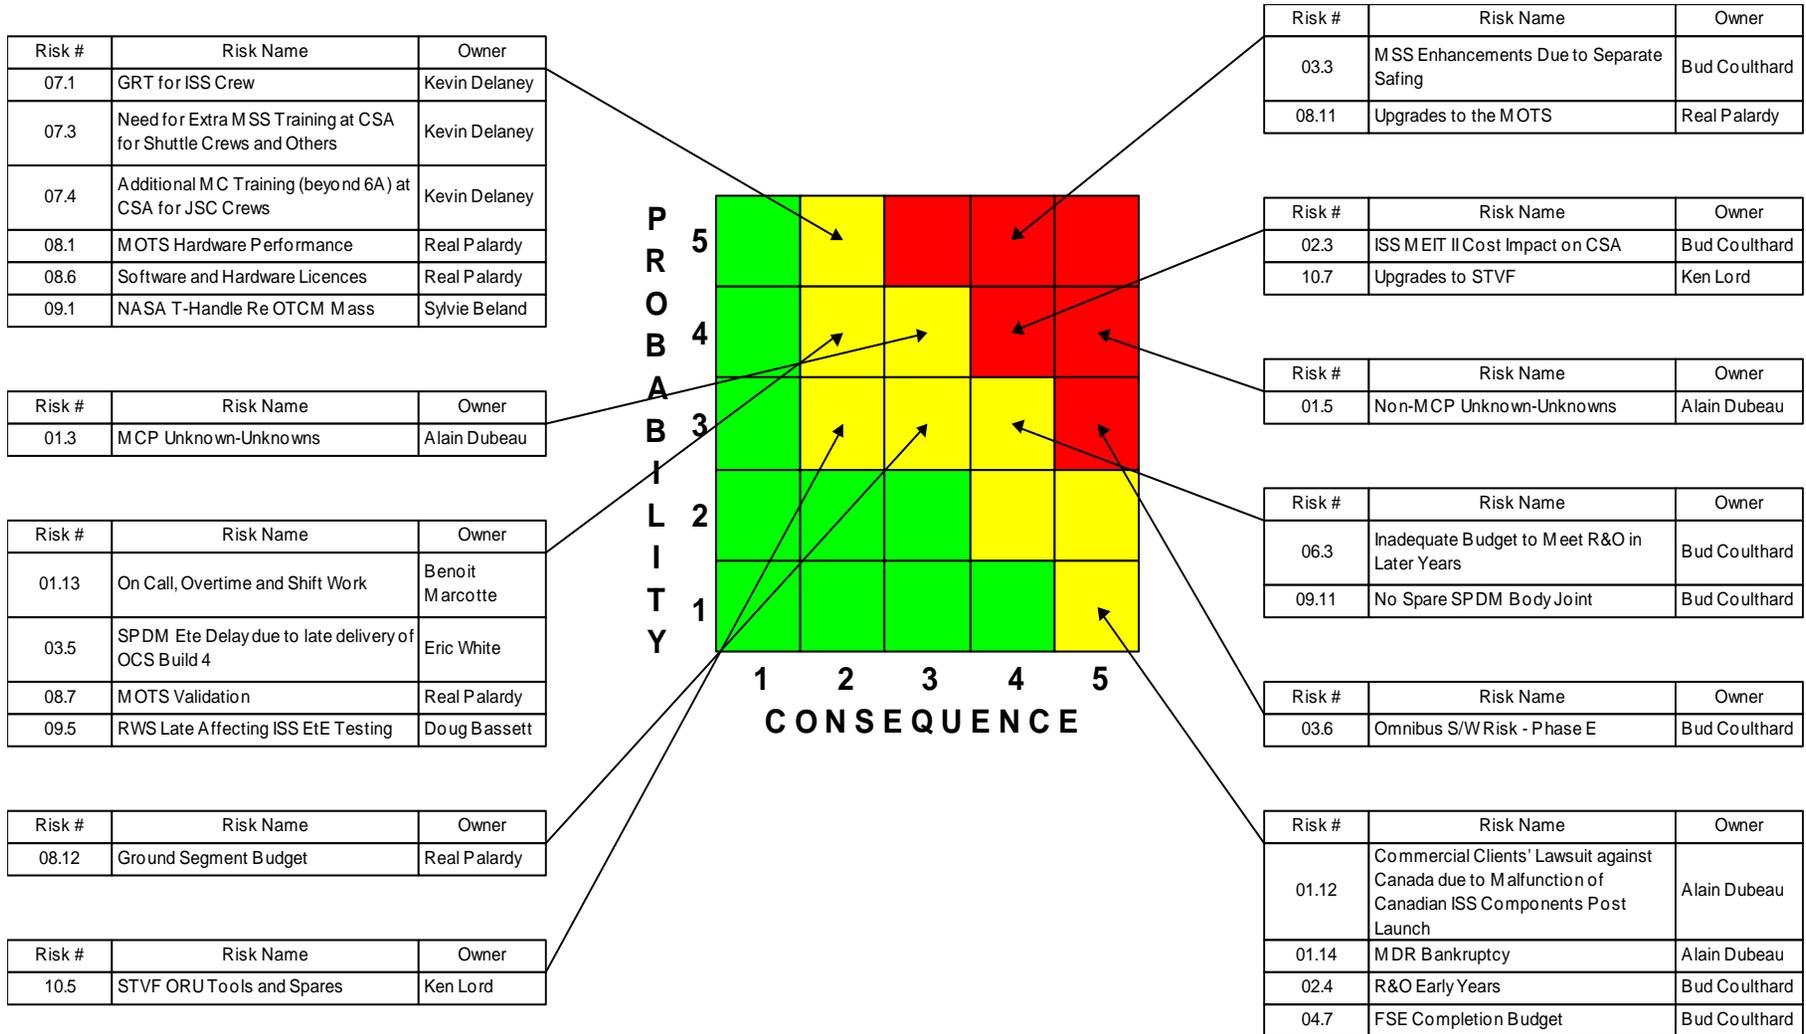

# CONSOLIDATED RISK ADVISORY BOARD



---

## CRAB AGENDA

- **Chair of Meeting:** Director General
- **Opening Remarks -**
  - ⌚ Level II Baseline as of October 24/01
- **Reports Attached**
  - ⌚ Risk Matrix: Red/Yellow Zone, CSSP MCP, Phase E, Short Term (01/02), Long Term
  - ⌚ Cost Reports: Unweighted Costs, Weighted Costs, Roll Up by Project
- **Update of LSE Plan Related to the CRAB Actions :**
  - ⌚ Risk 4.5 No Spare SSRMS Boom
  - ⌚ Risk 9.11 No Spare SPDM Body
- **New Risks**
  - ⌚ 1.16 Over Utilization of the MSS On-Orbit
  - ⌚ 3.11 OEUCS Memory Utilization
- **Conclusions and Recommendations**

# Five-Year Risk Assessment and Commitment Control Plan



- The Plan identifies risks and sources of frozen funds by program and project
- The Plan is continuously maintained up to date but formally reviewed by PRAB three times a year
  - ⌚ Work Plan (April)
  - ⌚ ARLU submission (August)
  - ⌚ Mid-year Performance Review (November)






Canadian Space Agency  
Agence spatiale  
canadienne



# Space: A National Resource for Canada



[www.space.gc.ca](http://www.space.gc.ca)

Canada
